

PROJECT DEVELOPMENT PACKAGE

Padang Besar Cross-Border Logistics Platform

Perlis, Malaysia · Malaysia–Thailand Border Corridor

Prepared for discussions with: **Government agencies · Investors · Shandong Hi-Speed Group · EPC contractors · Technology partners · Banks**

Draft for discussion · July 2026 · Prepared by the Prospek Ceraf project development team

This document asserts no ownership, concession, operating rights or licences. Items not publicly verified are marked “Pending confirmation from project owner.”

How this document was built — and what it does not claim

- Prepared by a multi-disciplinary development team covering project development, PPP/infrastructure, inland-port logistics, EPC, digitalisation, financial modelling, investment banking, risk, government relations and presentation design. Each specialist's output was cross-reviewed by the others before inclusion.
- Research base: publicly available sources only, verified as of 26 July 2026. Every factual statement in Section 2 carries a reference [R#], consolidated in the References appendix.
- Where public sources conflict (e.g., Perlis Inland Port capacity and cost figures), the conflict is disclosed rather than resolved by assumption.
- No site visits, data-room access or owner interviews have occurred. Nothing here should be read as confirmation of land, rights, mandates or approvals.
- All business models, work packages, structures and financial frameworks are proposals for negotiation — deliberately built so they can be validated or discarded item-by-item in due diligence.

DOCUMENT DISCIPLINE

- **Never fabricate facts**
- Separate fact tiers on every page
- Disclose source conflicts
- State what is unverified
- No numbers without evidence

Four information tiers — kept separate throughout

PUBLICLY VERIFIED

Facts supported by cited public sources (media, government, corporate disclosures). Each carries a reference [R#].

PENDING OWNER CONFIRMATION

Anything about this project's land, rights, mandates, agreements or status. Not asserted anywhere in this package.

PROPOSED

Business model, work packages, structures and strategies designed by the team — for negotiation, not statements of fact.

RECOMMENDATION

The team's professional judgment on sequencing, positioning and process — clearly separated from facts.

CONTENTS

Fifteen sections, one investment-grade narrative

01 Executive Summary

02 Public Research (referenced)

03 Current Ecosystem

04 Project Opportunities

05 EPC Work Packages WP01–WP20

06 Digitalisation Strategy

07 Prospek Cerah Business Model

08 Shandong Hi-Speed Role

09 Investment Model

10 Financial Model Framework

11 Due Diligence Checklist

12 Questions for Project Owner

13 Consortium Structure

14 Risk Register

15 Roadmap & Next Steps

+ Appendix: visual asset recommendations · assumptions register · consolidated references

01

- Why Padang Besar
- Why Malaysia
- Why border logistics
- Opportunities & challenges
- The honest bottom line

Executive Summary

Why Padang Besar, why Malaysia, why border logistics — and the one strategic question that must be answered before any capital moves.

Why Padang Besar: the corridor is real, growing and under-built

+25.9%

Padang Besar (Thai) checkpoint trade growth 2024 — 102.3bn baht, 3rd in Thailand for transshipment value [R48]

Only

direct Malaysia–Thailand rail link — juxtaposed customs inside the station [R2, R3]

~80%

utilisation of the 150,000 TEU legacy terminal before operations migrated [R15]

16 hrs

road border window (06:00–22:00) — a solvable structural constraint [R4]

Through this single crossing already run: **the electrified KTMB double-track corridor, the CMA CGM/Infinity Penang landbridge block trains, the ASEAN Express to Chongqing, and daily freight into the new Perlis Inland Port.** The infrastructure conversation at this border has already started — the question is who builds its next layer. [R10–R13]

Why Malaysia: a policy machine is already funding this corridor

US\$30bn

official Malaysia–Thailand trade target for 2027, with a joint trade-facilitation task force [R46]

PIKAS 2030

national PPP master plan: RM78bn private investment target, competitive RFP model [R61]

NCIA / NCER

statutory development authority for Perlis with logistics as a mandated sector [R56]

~RM400m

government external works already delivered at this border (bonded road, rail spur, flyover) [R23, R36]

RM374m

Bank Pembangunan financing approved for Perlis Inland Port — lender precedent at this exact location [R25]

Border Economic Zone

announced by both Prime Ministers, July 2026 — spanning the northern border states [R60]

Malaysia pairs this policy stack with a common-law system, deep sukuk/project-finance markets, and institutional lenders (BPMB, AIIB partnerships with Maybank/CIMB/AmBank) active in exactly this asset class. [R80]

Why border logistics: chokepoint economics with a rail growth option

- Land-border trade is ~40% of US\$25bn bilateral trade (2024) — and this checkpoint grew +25.9% while the total grew single digits. [R47, R48]
- Border logistics is a chokepoint business: where two customs regimes, two rail operators and two road networks meet, every improvement in flow is monetisable — handling, storage, marshalling, data.
- Cross-border flows are the least commoditised, highest-friction segment of ASEAN logistics — friction is the revenue pool.
- The China–ASEAN rail narrative (ASEAN Express since 2024; Kunming–Singapore corridor phases to 2031) adds a structural growth option on top of the bilateral base. [R12, R54]
- ~70% of southern Thailand's export cargo already transships through Penang — the landbridge through Padang Besar is its land leg. [R51]

WHY NOW

- PIP operating + FCZ live (May 2026): ecosystem momentum
- SRT Hat Yai–Padang Besar double-tracking at bid stage [R35]
- Border Economic Zone incentives being defined now
- 13MP road-to-rail push; KTMB volumes +23.5% YoY [R33, R34]
- Positioning windows close once corridors consolidate

The honest bottom line — and the strategic question

WHAT IS VERIFIED

- The corridor: trade volumes, growth, rail services, policy support
- The precedents: PIP financing, Thanaleng model, Shandong Hi-Speed active in Malaysia
- The constraints: border hours, Thai single-track, competition

WHAT IS NOT VERIFIED

- This project's land, rights, mandate and approvals
- Its relationship to the operating Perlis Inland Port
- Any commitment by Shandong Hi-Speed, government or investors

THE STRATEGIC QUESTION

Perlis Inland Port is operating in the same town — state-backed, KTMB-run, royally launched. This project must define itself as **integration, complement, or competitor** to PIP before approaching any investor. This package is built to force that answer early (Sections 11–12), then convert the verified corridor thesis into an investable transaction (Sections 13–15).

02

Public Research

Only publicly verifiable information, every statement referenced. Conflicting sources are disclosed; unverifiable items are quarantined.

- Border & rail anatomy
- Perlis Inland Port
- Trade statistics
- Policy & stakeholders
- What we could not verify

The border system: one town, two regimes, three channels

Channel	Verified facts	Refs
Rail	Malaysia's only direct rail link with Thailand. Station (1918) hosts juxtaposed MY+TH border controls. KTMB electrified double-track metre-gauge line meets SRT Southern Line. No gauge break — both networks are metre gauge; the standard-gauge break for China traffic is at Thanaleng, Laos.	R2, R3, R9, R30
Road	ICQS complex handles passenger + cargo vehicles; hours ~06:00–22:00 (not 24h). Federal Route 7 starts at the border; FT79 links south; expressway via Changlun. The busier road crossing is Bukit Kayu Hitam–Sadao, 45 km east — new link road opened July 2026.	R4, R6–R8, R42, R43
Customs	JKDM/RMCD administers the land entry point. National digital rails: uCustoms/SMK; ASEAN Single Window live for e-Form D across all 10 member states. ACTS transit system piloted by MY–SG–TH. Single-stop inspection studied (CAREC), implementation unverified.	R18, R21, R44, R45

Detail slide 3.2 maps these channels as a flow diagram.

Rail cargo: four services already run through this crossing

KTMB Kargo landbridge

Container services linking Penang Port, Port Klang and Padang Besar; ~4-day transit concept. [R10]

Penang block train (2022)

CMA CGM / Infinity Penang–Padang Besar service; corridor reported up to 7,500 TEU/month. [R11]

ASEAN Express (2024)

KL (Kontena Nasional ICD) → Padang Besar → Lat Krabang → Thanaleng → Chongqing. ~9–14 days vs 14–21 by sea. [R12, R31]


STC Perai–PIP (2025)

Daily freight into Perlis Inland Port; first train 80 TEU on 1 Dec 2025. [R13]

Capacity outlook

- 13MP-era plans: Padang Besar Depot upgrade, road-to-rail shift, North Butterworth terminal upgrade [R33]; KTMB rail volumes +23.5% YoY Jan 2026 [R34]
- Thai side: SRT double-tracking Hat Yai–Padang Besar (45 km, ~7.77bn baht) slated for bidding within 2026 [R35]

Perlis Inland Port: the operating incumbent next door

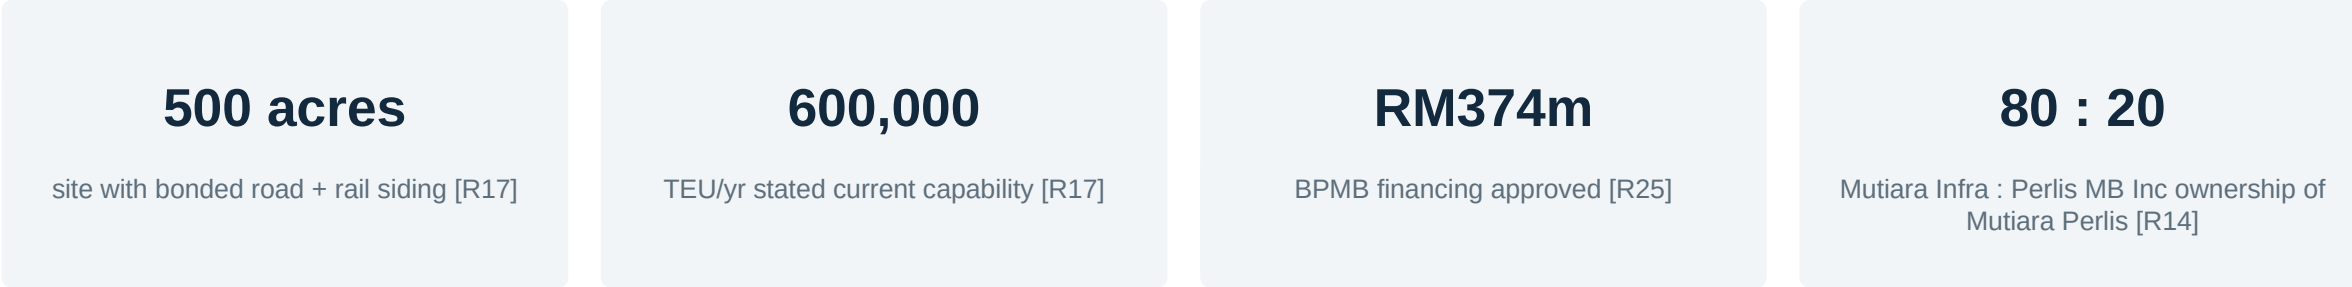

Disclosed source conflicts: total cost reported between RM327m and RM492m across outlets; ultimate capacity reported as both 1M and 2M TEU/yr. Figures used here are the best-attested official statements. [R17, R26, R27, R37, R38]

Malaysia–Thailand trade: the demand base is verified

US\$25.06bn

bilateral trade 2024; ~40% via land borders
[R47]

US\$30bn

official 2027 target (3rd Joint Trade Committee)
[R46]

102.3bn baht

Padang Besar checkpoint 2024, +25.9% YoY
[R48]

315.1bn baht

Thai–Malaysia border trade 2025 — Thailand's
largest border partner [R49]

What moves across this border

- Exports through Sadao/Padang Besar led by hard disk drives and processed wood; rubber (TSNR) via Songkhla checkpoints +39.3% [R48]
- F&B reported as the largest cross-border category, followed by E&E (single source) [R50]
- Sadao handles ~2× Padang Besar's trade value — but Padang Besar is growing far faster and owns the rail channel [R48]
- ~70% of southern Thailand's export cargo transships via Penang — the corridor this platform would serve [R51]

Government initiatives: federal, state and bilateral layers

Layer	Initiative	Relevance	Refs
Bilateral	US\$30bn 2027 target + task force; Border Economic Zone announced Jul 2026; new BKH–Sadao road opened	Political momentum for border trade infrastructure	R46, R60, R42
Federal	PIKAS 2030 PPP master plan; National Transport Policy 2019–30; 13MP road-to-rail + Padang Besar Depot upgrade; NIMP 2030 (logistics as enabler)	Defines the PPP route (UKAS RFP), rail investment pipeline	R61, R58, R33, R59
Regional	NCIA (Act 687) mandate for NCER; Chuping Valley Industrial Area (2,482 acres, green/halal); IMT-GT corridor	The statutory sponsor that already co-funded PIP external works	R56, R57, R53
State	Perlis investment drive (MIDA Invest Series 2025); Padang Besar designated growth area; largest-ever state budget 2026	State government actively courting logistics investment	R39, R64, R65
Ownership rules	≥51% Malaysian ownership floor for port/strategic concessions (reaffirmed Jul 2026); Bumiputera equity conditions in logistics licensing	Hard constraint on consortium design (Section 13)	R62, R63

The Thai side: capacity is coming toward this border

- **SRT southern double-tracking package includes Hat Yai–Padang Besar (45 km, ~7.77bn baht) — explicitly framed as strategic for the Malaysia corridor; bidding targeted within 2026. [R35]**
- Thai CIQ upgrade plans reported at Padang Besar (single source — scope/budget unpublished). [R20]
- New Sadao CIQ–Bukit Kayu Hitam road opened 10 July 2026 (11 vehicle + 14 immigration lanes/side, dual X-ray cargo terminal) — strengthens the competing road corridor. [R42]
- Songkhla is southern Thailand's logistics province: rubber, wood, seafood export base; Padang Besar (Thai) station is the Southern Line freight terminus. [R48]
- Thai Land Bridge (Chumphon–Ranong) remains in study flux — fresh environmental studies ordered June 2026; a long-run variable, not a near-term constraint. [R55]

READ-THROUGH

Rail capacity into Padang Besar is being doubled from the Thai side while road capacity consolidates at Sadao–BKH. A rail-centred platform at Padang Besar aligns with where both governments are putting steel.

Stakeholder map: who already acts in this corridor

Cluster	Stakeholders (published roles)	Refs
Federal	MOT (rail/logistics policy; PIP champion) · MITI/MIDA (trade target, promotion) · JKDM Customs · UKAS (PPP gatekeeper) · Railway Assets Corporation	R33, R46, R61
Regional/State	NCIA (external infra funder, CVIA developer) · Perlis state govt & MB Inc (20% of Mutiara Perlis) · Padang Besar growth-area designation	R14, R23, R56, R65
Rail & ports	KTMB (ASEAN Express, PIP O&M, TKPB) · SRT (Southern Line, double-tracking) · Penang Port (70% of southern-Thai transshipment) · Kontena Nasional (ASEAN Express origin ICD)	R12, R16, R35, R51
Corporate	Mutiara Perlis / Perlis Inland Port Sdn Bhd · Maersk (MOC) · CMA CGM/Infinity (block train) · Citaglobal, Berjaya Property (equity moves) · Kalmar (equipment)	R11, R22, R39, R41
Thai side	Thai Customs (Padang Besar & Sadao houses) · SRT · Songkhla province · Thai MOT/OTP	R35, R42, R48

What we could not verify — quarantined from all argumentation

- Ultimate PIP capacity (1M vs 2M TEU/yr) and total PIP cost (RM327m–RM492m across outlets) — conflicting public figures
- Malaysian checkpoint-level trade statistics (JKDM does not publish; Thai customs data used instead)
- Free Commercial Zone gazettelement instrument; bonded warehouse licences at PIP
- uCustoms operational status at Padang Besar specifically; single-stop inspection implementation
- Any route designated “R15” serving Padang Besar (referenced in early briefs — no such designation found)
- Current Shandong Hi-Speed parent credit rating; Chinese trade-press claims of “>RMB 60bn Malaysia orders”
- Any MMC Corporation involvement in PIP; any SDHS/CSI mandate in Perlis
- Rail share of bilateral trade; ASEAN Express cumulative volumes
- Border Economic Zone boundaries and incentives (announced July 2026; details unpublished)

Rule applied: anything on this list is excluded from the business case and routed to due diligence (Section 11) or owner questions (Section 12).

03


- Corridor flow map
- Border process flows
- Facility inventory
- Ecosystem gaps

Current Ecosystem

How cargo actually moves through Padang Besar today — road, rail, warehouse, container, cold chain, border and customs.

Corridor flow: how the pieces connect

THAILAND · Songkhla

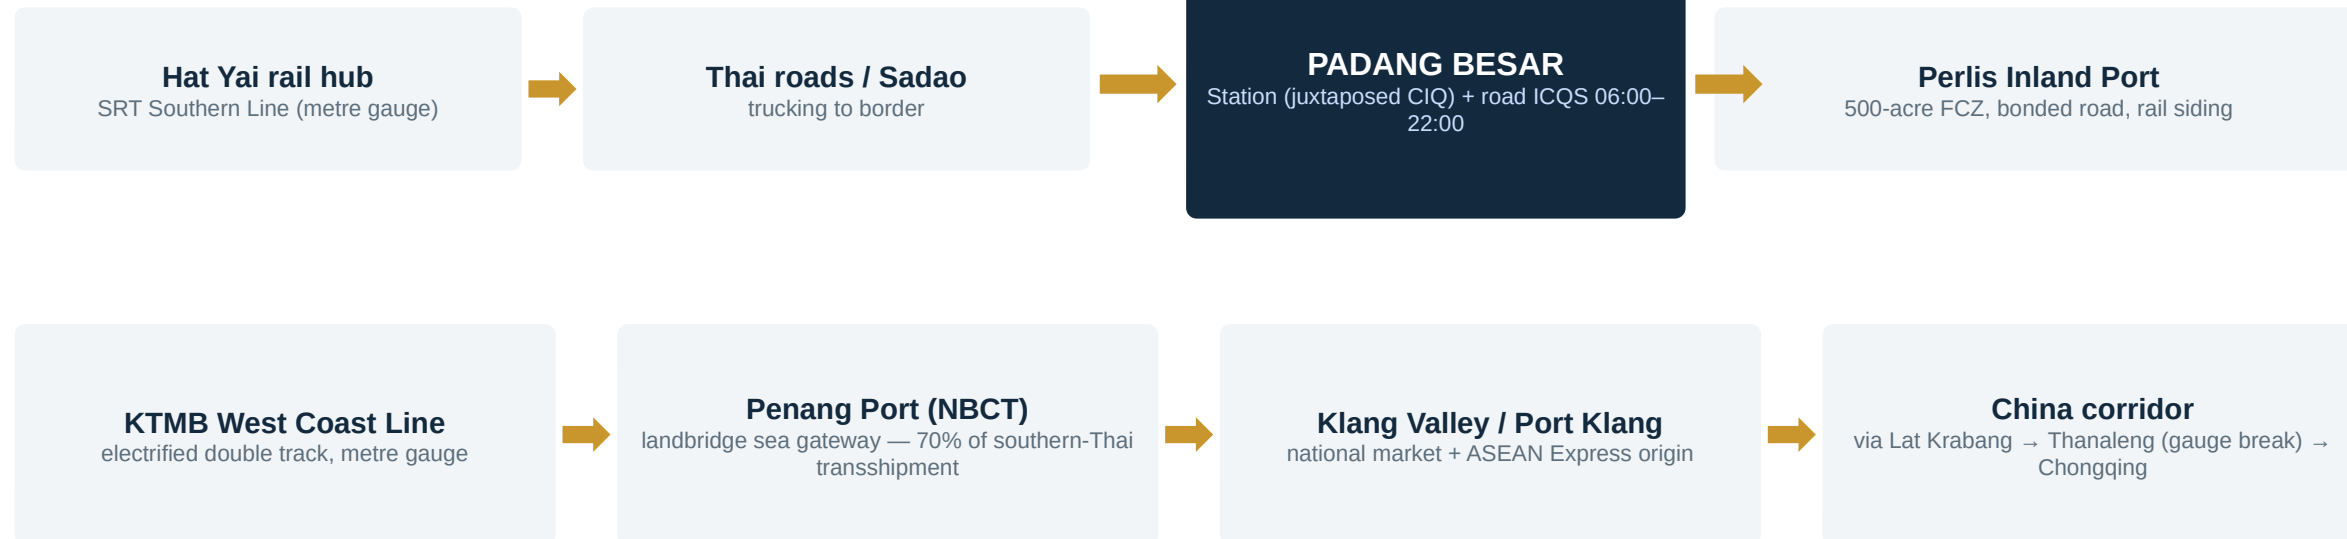


Key structural facts


- No gauge break at this border (both metre gauge) — rail interchange here is commercial, not technical [R9, R30]
- Road cargo constrained by the 16-hour border window; heavy road flows consolidating at Bukit Kayu Hitam–Sadao [R4, R42]

Border process: rail vs road today

RAIL CARGO (juxtaposed controls)



ROAD CARGO (sequential controls, 06:00–22:00)



The friction points are visible: unmanaged truck queues against a hard 22:00 cutoff, paper-heavy road clearance, and no published integrated visibility from booking to release. Rail avoids most of this — which is why the corridor's growth is running through it. (Team interpretation based on referenced facts.)

Facility inventory: what exists at the border today

Element	Current state (published)	Refs
Container terminal	Legacy TKPB: 150,000 TEU/yr, ~80% utilised before migration; operations moved to PIP 12 Apr 2026	R15, R16
Inland port / FCZ	PIP: 500 acres, 600,000 TEU/yr capability, bonded road, rail siding, FCZ launched 30 May 2026	R17
Warehousing	PIP warehousing targets halal, automotive, rubber; no other large modern stock documented at the border	R14
Cold chain	No large-scale multi-user cold-chain facility documented in public sources — apparent white space (interpretation)	—
Truck facilities	No managed marshalling/booking system documented; border hours 06:00–22:00	R4
Customs facilities	ICQS complex (road) + juxtaposed controls (rail); Thai CIQ upgrade plans reported (single source)	R3, R20
Handling equipment	PIP: RM17m Kalmar order (15 units) via Mach 1, May 2025	R36

Ecosystem gaps: five white spaces (team interpretation)

1

Cold chain at scale

Perishables flow both ways (Thai fruit/seafood south, Malaysian halal north) with no documented multi-user cold facility at the border.

2

Truck marshalling

A hard 22:00 cutoff with unmanaged queues = monetisable slot booking, secure parking and call-up services.

3

Digital corridor visibility

No published integrated system links booking → gate → customs status → release across the crossing.

4

Free-zone VAS

Labelling, kitting, halal certification support and light processing inside zone conditions — early-stage at PIP.

5

24-hour operations

A bilateral policy matter, repeatedly raised, unresolved — the single biggest unlock, outside private control.

These five gaps are the demand hypotheses the feasibility study must test — they are interpretations, not established markets.

04

- Construction scope
- Operations & commercial
- Asset management
- Expansion & digital

Project Opportunities

The opportunity map across the platform lifecycle — construction, operations, commercial, asset management, expansion, digital.

Build & operate: the physical opportunity set

Construction (◆ = needs land/rights, ● = needs govt/agency agreement)	Operations
Site development & flood-resilient earthworks ◆	Terminal operations: rail yard + container yard (self-perform or operator partner)
Warehouses: ambient, bonded, cold chain — smart-warehouse spec ◆	Warehouse operations: 3PL contracts, bonded ops, cold-chain management
Rail sidings & terminal trackworks (KTMB agreement) ◆●	Truck terminal: marshalling, booking slots, secure overnight parking
Internal roads, truck marshalling infrastructure ◆	Facility management, security, equipment maintenance & rental
Utilities: substations, water, fire, solar PV, standby power ◆	Reefer pre-trip inspection, container repair & washing
Buildings: admin, commercial, customs/agency facilities ◆●	Border-services support offered to agencies (inspection support) ●
Digital infrastructure built with civil works, not retrofitted ◆	Energy services: solar PPA, energy-as-a-service for cold tenants

Precedent: the SDHS–PTT Synergy smart-warehousing framework (Sep 2025) shows the build model is already active in Malaysia. [R72, R73]

Commercial, asset management and digital layers

COMMERCIAL

- Anchor leasing: 3PLs, forwarders, Thai & Malaysian shippers, e-commerce
- Free-zone VAS: labelling, kitting, halal support, light assembly ●
- Trade services cluster: brokers, banks, insurers, surveyors as tenants
- Fuel, retail, F&B concessions serving driver traffic

ASSET MANAGEMENT

- ISO 55000 regime as a paid service to the SPV and zone tenants
- Capex renewal programme management over a 30+ year life
- Energy management and solar PPA structures
- Digital-twin-driven lifecycle optimisation (Section 6)

DIGITAL

- Corridor visibility platform: booking → gate → customs → delivery
- Data products for shippers, forwarders and agencies
- Smart-warehouse services on SDHS-ecosystem automation
- Command-centre services to tenants and, potentially, agencies ●

● = requires government/agency agreement — routed to Section 12 owner questions and Phase 1–2 engagement.

Expansion options: what Phase 2+ can become

E-commerce fulfilment campus

Riding cross-border e-commerce growth on the rail corridor

Halal logistics hub

Aligned with Chuping Valley Industrial Area's halal-industry positioning • [R57]

Cold-chain corridor scaling

Growing with Thai perishables and Malaysian halal exports

Standard-gauge readiness

Passive provision if Pan-Asian rail plans ever extend south •

Model replication

Apply the platform + digital playbook at other crossings (Rantau Panjang, Bukit Kayu Hitam)

Border Economic Zone play

Participate once incentives are gazetted (announced Jul 2026) • [R60]

All expansion options are design-stage provisions only — safeguarded land and corridors (WP20), not committed scope.

05

EPC Work Packages

Twenty packages structured for consortium scope allocation, staged financing and early-revenue sequencing. Scope and siting pending owner confirmation.

- WP01–04 Enabling
- WP05–10 Core logistics
- WP11–14 Buildings & border
- WP15–17 Digital
- WP18–20 Readiness & expansion

WP01–WP10: enabling works and core logistics infrastructure

WP	Package	Scope highlights
WP01	Site investigation & surveys	Topo/geotech/hydrology, utilities, boundary, environmental & social baseline, border traffic counts
WP02	Enabling works & earthworks	Clearance, cut-and-fill, ground improvement, platform formation, construction drainage
WP03	Utilities & services	Power intake + substations (TNB), water, sewerage, telecom ducting, fire systems, standby power, solar provision
WP04	Roads, drainage, landscape	Internal heavy-duty pavements, stormwater + flood mitigation, fencing, buffers
WP05	Rail siding & trackworks	Sidings to KTMB corridor (subject to agreement), turnouts, terminal pavement — no gauge break exists; passive future-gauge provision only
WP06	Rail systems & signalling	Terminal signalling, main-line interlocking interface, rail weighbridge-in-motion
WP07	Container yard & intermodal	Paved yard, reefer racks, handling equipment, yard lighting/CCTV masts
WP08	General & bonded warehousing	Ambient + bonded zones with customs-compliant segregation, docks, VAS areas
WP09	Cold chain facilities	Multi-temperature rooms, blast freezing, insulated docks, halal-compliant segregation
WP10	Truck terminal & inspection	Marshalling yards, queue lanes, weighbridges, driver amenities, inspection canopies

WP11–WP20: buildings, digital systems and readiness

WP	Package	Scope highlights
WP11	Customs & agency facilities	Office/inspection space offered to JKDM, MAQIS, Immigration; scanner foundations (scanners typically govt-procured — TBC)
WP12	Admin & commercial buildings	HQ, tenant offices (forwarders, brokers, banks), canteen, surau, clinic, training
WP13	Workshops & MRO	Container repair/washing, equipment workshops, reefer PTI stations
WP14	Security infrastructure	Bonded-grade perimeter, access control, guardhouses, secondary inspection areas
WP15	Terminal operating system	TOS + rail planning module, EDI with KTMB/lines/haulers, gate integration
WP16	WMS, billing & ERP	Ambient/bonded/cold WMS, billing engine, customer portal, customs-system interfaces (subject to JKDM availability)
WP17	Site-wide digital infrastructure	Fibre, private wireless, data centre, IoT, ANPR, AI CCTV, command centre, digital twin, cyber stack
WP18	Testing & operational readiness	Integrated testing, dry runs with hauliers/forwarders, customs rehearsal, hiring & SOPs
WP19	Taking-over & defects	Certification, punch lists, as-builts, digital twin handover
WP20	Future expansion provision	Safeguarded land/utility corridors for Phase 2+ — passive design provision only

Packaging strategy: how the WPs go to market

- **Single EPC wrap preferred.** A fixed-price, date-certain EPC head contract over WP01–WP14 (+WP17 build) is the lender-friendly route; nominated subcontracts for rail systems and digital where specialists differ.
- Rail packages are schedule-critical. WP05–WP06 need KTMB technical approval and possession planning — engage before EPC pricing, and design the platform to open road-only if rail consent lags.
- Split-out option: WP15–WP17 as a systems-integrator contract under Prospek's integration accountability, if the technology consortium differs from the civil EPC.
- Long-lead items to order early: refrigeration plant (WP09), handling equipment (WP07), substation equipment (WP03), scanners/ANPR (WP17).
- Local content is structural, not optional: CIDB registration, Bumiputera contractor programmes and Malaysian subcontracting shape the EPC consortium from day one. [R62, R63]

SEQUENCING LOGIC

WP01–04
enabling



WP05–10
core

WP11–14
buildings



WP15–17
digital

WP18–19
readiness



WP20
expansion

06

Digitalisation Strategy

The most digitally advanced land-border logistics facility in ASEAN — where the data layer is a revenue line, not a cost line.

- Five-layer architecture
- Sixteen capability modules
- Command centre & cyber
- Phasing & digital revenue

Five-layer architecture: field sensors to revenue insight

L5 · INSIGHT & REVENUE

Integrated dashboard · digital twin analytics · data products · ESG reporting

L4 · APPLICATIONS

TOS · WMS · truck management/VBS · asset management (EAM) · billing · customer portal

L3 · PLATFORM

Digital twin core (GIS + BIM) · IoT platform · video analytics · data lake · API/EDI bus

L2 · NETWORK

Fibre backbone · private 4G/5G · LoRaWAN · redundant WAN · edge compute

L1 · FIELD

AI CCTV · ANPR · IoT sensors · drones · weighbridges · RFID/OCR gates · smart meters · access control

Open standards at every layer — no vendor lock-in; Chinese, Malaysian and international vendors compete at subsystem level.

Capability modules (1 of 2): the built environment goes digital

Digital Twin

Live 3D model fusing GIS + BIM + IoT: design coordination → operations simulation → asset lifecycle

GIS

Land parcels, utilities, flood modelling, corridor and expansion planning

BIM

Level 2+ mandated across design (CIDB-aligned); CDE from day one; BIM-to-FM handover

Drones

Construction photogrammetry, volumetrics; then perimeter patrol and stack audits (CAAM permits)

IoT

Reefer telemetry, cold rooms, energy submetering, pavement/structure and flood sensors

AI CCTV

Safety (PPE, intrusion), security (perimeter), operations (dock occupancy, queue estimation)

ANPR

Malaysian + Thai plates at all gates; links truck identity to bookings and customs status

Predictive maintenance

Telematics + EAM condition-based maintenance for equipment, refrigeration, substations

Capability modules (2 of 2): operations, flow and trust

Command Centre (ICC)

One control room: CCTV walls, TOS/WMS status, gates, border queue dashboard, incident management; hosts agency liaison desks

Warehouse automation

Phased: WMS-directed → RFID/barcode → conveyor/sortation and AMRs in e-commerce zones

Truck management (TMS/VBS)

Slot booking, driver app (BM/Thai/EN/CN), e-call-up, release tied to customs status

Smart parking

Occupancy sensing for marshalling + staff parking; dynamic signage; paid overnight parking

Traffic analytics

Queue length, dwell, lane throughput — shareable with police/JKR/customs

Asset management (EAM)

ISO 55000 register, lifecycle costing — underpins the long-term asset management services role


Integrated dashboard

Board/agency KPI layer: TEU, dwell, revenue, energy, safety, ESG — investor-grade reporting


Cybersecurity

IEC 62443 (OT) + ISO 27001 (IT), segmented customs-facing systems, SOC, Cyber Security Act 2024 compliance, PDPA

Phasing and the digital revenue logic

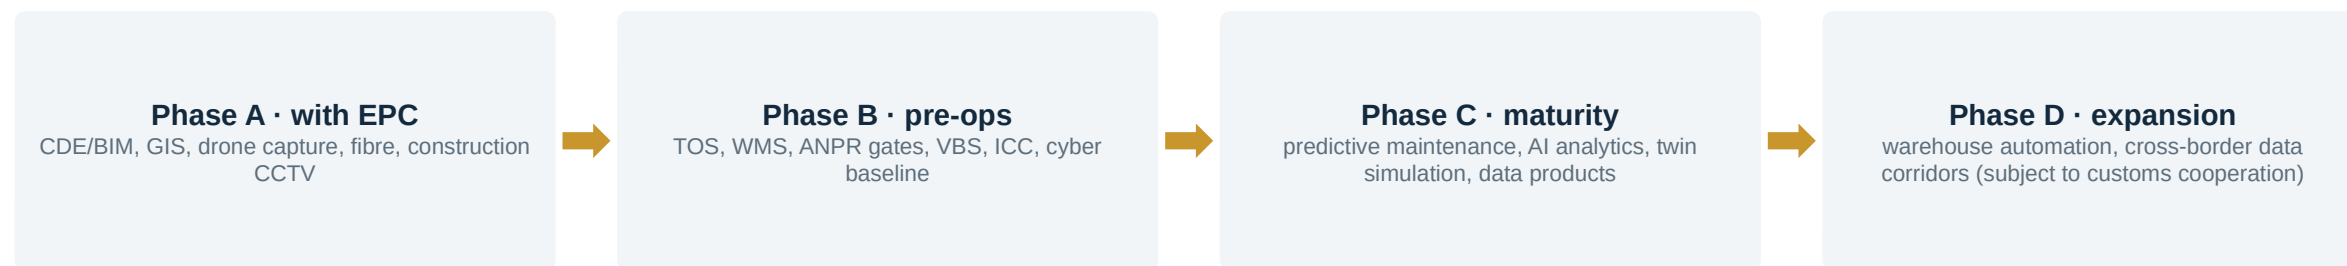

Digital as a revenue line (categories only — quantification pending feasibility, Section 10)

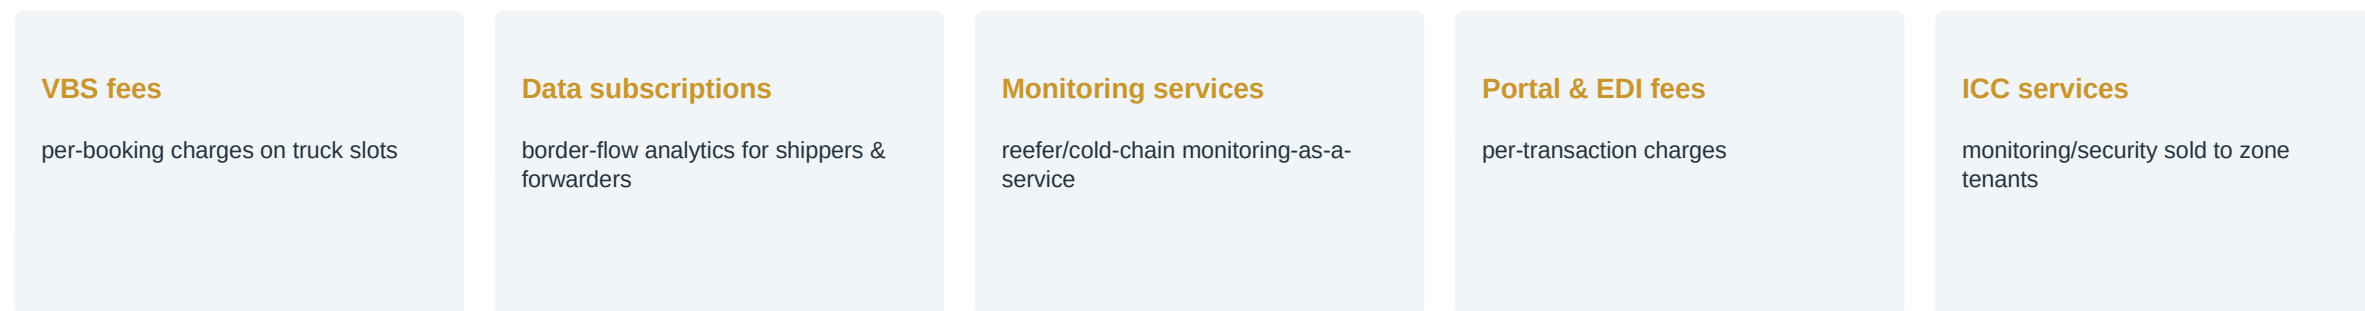

Principle: every digital system must either cut border dwell time or create a recurring income line — ideally both.

07

- Why not a broker
- Eight roles
- Lifecycle fit
- Governance position

Prospek CERAH Business Model

Not a broker: a developer with capital at risk, contracted deliverables and income that arrives only if the project is built and operates well.

Why Prospek CERAH is not a broker

Dimension	Broker	Prospek CERAH (proposed)
Time horizon	Transaction close	Full lifecycle: development → operations → expansion
Accountability	None after introduction	Contracted deliverables: milestones, PMO KPIs, digital SLAs
Capital	No skin in the game	Development capital at risk pre-financial-close; proposed SPV equity
Value creation	Access	Project definition, structuring, integration, delivery capability
Revenue	One-off commission	Milestone-earned fees + long-term recurring income
Relationships	Introduces, then exits	Holds and manages stakeholder relationships permanently

The economic point for partners: the majority of Prospek’s proposed income arrives only if the project is built and operates well.

Eight roles across the project lifecycle

1 · Project Developer

Originates and defines the project; funds pre-development; carries risk to financial close

2 · Consortium Builder

Assembles SPV shareholders, EPC, technology, operator, financiers as one integrated package

3 · Business Development

Builds the cargo book: shipper pre-commitments, anchor tenants, Thai counterparts

4 · PMO

Owner's-side programme management across WP01–WP20: schedule, cost, risk, lender reporting

5 · Technology Integrator

Accountable for WP15–WP17 systems working together and with government systems

6 · Digitalisation Partner

Long-term operator of the digital layer under SLA — recurring service income

7 · Asset Management

ISO 55000 management of the asset across its life; handback compliance if concession applies

8 · Strategic Partner

Standing counterpart to owner, state, federal and Shandong for expansion and replication

Develop (Yr 0–2): roles 1–3 · Deliver (Yr 2–5): roles 4–5 · Operate (Yr 5+): roles 6–8. Governance: SPV shareholder + contracted PMO + digital/AM services — all related-party contracts disclosed and market-benchmarked.

08

- Verified profile
- Strategic fit
- Scope options
- Commercial postures

Shandong Hi-Speed Role

What SDHS could undertake — structured for negotiation. No commitment by SDHS exists; corporate facts are referenced.

Verified profile: scale, rail logistics and live Malaysia activity

>9,000 km

expressways operated — provincial SOE, HQ Jinan [R66, R68]

RMB 1.76tn

reported total assets; Fortune Global 500 #401 (company-published — cross-check in DD) [R67]

Qilu Express

China–Europe freight brand; 2,500 Shandong-handled trips in 2023 [R69]

RMB ~70bn

revenue of listed EPC arm Shandong Hi-Speed Road & Bridge (000498.SZ) [R70]

- **Live in Malaysia: framework agreement with Bursa-listed PTT Synergy (23 Sep 2025) for smart/automated warehousing — reported ~RM2bn (Malaysian media) vs RM6bn/2M pallet positions (Chinese trade press); discrepancy disclosed. [R72, R73]**
- China Shandong International (CSI), wholly-owned since 2008, has a Malaysian-registered entity. [R71]
- Ratings: Moody's first-time A3 (2018; current parent rating not publicly confirmable); Fitch A – /Stable on HK-listed Shandong Hi-Speed Holdings. [R74]
- **No published SDHS commitment to Perlis or Padang Besar exists — the role described in this section is proposal-stage only.**

Scope SDHS could undertake — and three commercial postures

Domain	Potential SDHS scope	WPs
Civil & infrastructure	Earthworks, roads, pavements, rail sidings & systems (with KTMB approval), utilities	WP02–07, 10
Warehousing & buildings	Ambient/bonded/cold warehouses; customs, admin, commercial buildings; workshops	WP08–09, 11–13
Digital & ICT	Site-wide digital infrastructure delivery; fibre, data centre — under Prospek integration	WP15–17
Operations & maintenance	Terminal O&M participation via logistics arms; long-term infrastructure maintenance	Ops phase
Future expansion	EPC for Phase 2+; potential co-investment in expansion capex	WP20

Posture 1

EPC contractor only — date-certain, price-certain wrap; simplest entry

Posture 2

EPC + SPV equity — aligns delivery and ownership; needs related-party safeguards

Posture 3

EPC + equity + O&M — deepest integration; shares operating risk and upside

SDHS internal-approval needs: verified land/rights, bankable feasibility, tenure clarity, governance framework, CIDB licensing and Chinese outbound approvals (NDRC/MOFCOM/SAFE).

09

Investment Model

Investor universe, revenue streams, capital and equity structure, PPP options, risk allocation, funding stages and exits — structures only, no invented numbers.

- Investor universe
- Revenue streams
- Capital & PPP structure
- Risk allocation & exits

The investor universe — and what each needs to see

Investor category	Examples of type	What they need to see
Strategic — construction/infra	Shandong Hi-Speed Group and peers	EPC pipeline + equity upside; government endorsement
Strategic — logistics operators	Terminal operators, rail logistics groups, 3PLs	Operating control or strong agreements; cargo commitments
Logistics real estate platforms	Regional industrial developers & funds (e.g., LOGOS-type JVs) [R81]	Leasable product, tenant covenants, yield profile
Financial — infrastructure funds	ASEAN/Asia infra and PE funds	Contracted revenue share, credible exit, governance rights
Malaysian institutions	GLIC/pension-type investors (mandate-dependent)	National-interest alignment, stable yield, local partner quality
DFIs / policy lenders	IFC, AIIB, ECAs, policy banks — Thanaleng precedent [R75, R76]	ESG compliance, trade-facilitation impact, sovereign context
State/federal vehicles	State economic corporations, facilitation funds	Jobs, state revenue, border modernisation outcomes

Revenue architecture: six stream families

CORE TERMINAL

Rail handling · container lift/storage · transshipment · reefer plugs · empty depot

WAREHOUSING

Ambient/bonded/cold leasing · VAS (kitting, labelling) · e-fulfilment

BORDER SERVICES

Truck marshalling/slot fees · weighbridge · inspection support · paid parking

COMMERCIAL

Office/retail rents · fuel & service concessions · advertising

DIGITAL

VBS fees · data products · reefer monitoring · portal transaction fees

DEVELOPMENT & MGMT

PMO fees · asset management fees · expansion development fees (accrue to service providers, not SPV)

No stream is quantified in this package: each enters the lender base case only with an identified contractual or statistical basis (Section 10).

Capital structure logic and PPP model options

CAPITAL STACK (logic, no figures)

Senior debt

Project finance sized on contracted revenue — BPMB precedent at PIP; AIIB–Malaysian bank platforms; ECA cover; sukuk-capable [R25, R80]

Mezzanine

Optional gap layer from strategic sponsors

Sponsor equity

Consortium equity, staged against milestones

Govt support

To be explored, never assumed: tenure, incentives (MIDA/zone), facilitation funding [G]

PPP MODEL OPTIONS (depends entirely on true land position)

Model	When it fits
Private land, build-own-operate	Land privately held; licensed private facility
State land lease + BOT/BOO	State land; requires state agreement
Concession incl. agency facilities	Government wants integrated border facilities (WP11)
Hybrid landlord model	SPV as landlord; specialist operators as tenants — reduces operating risk

PIKAS 2030 preference: competitive RFP and user-pays projects — engagement route via UKAS if any government facility/concession element applies. [R61]

Risk allocation, funding stages and exit options

Risk	Allocated to	Instrument
Construction	EPC contractor	Fixed-price date-certain wrap, LDs, performance security
Cargo / market	Shared	Anchor pre-commitments + sponsor equity buffer
Operating performance	Operator	KPI-linked O&M contract with step-in rights
Border policy / customs	Not transferable	Government engagement; diversified revenue mix
Land / approvals	Development phase	Precondition to financial close — never carried by lenders

EXIT OPTIONS

- Trade sale to strategic operator or logistics RE platform
- Infra fund sale once cash flows season
- REIT injection of stabilised warehouse assets
- IPO of the platform company at scale
- Refinancing for partial sponsor liquidity



10

- Modelling principles
- Revenue categories
- Cost categories & sensitivities
- Outputs per audience

Financial Model Framework

Deliberately no invented numbers. The model structure and every assumption class that must be evidenced before a single figure is entered.

Modelling principles and revenue categories (no figures)

Every input traces to evidence · three cases minimum (base/downside/upside) · MYR model with THB/USD/CNY sensitivity · no revenue in the lender case without a contractual or statistical basis

Category	Potential lines (to be quantified only after evidence)
Terminal & rail	Rail handling per TEU · storage & empty depot · reefer plugs · wagon/shunting services (KTMB commercial terms pending)
Warehousing & property	Ambient rents · bonded premiums · cold chamber/pallet/blast-freeze · built-to-suit returns · sub-lease income (tenure permitting)
Border & vehicle services	Marshalling slots · secure parking · weighbridge · driver amenities & concessions
Operating income	Handling labour, VAS · customs brokerage facilitation (licensing pending) · equipment rental
Recurring income	Multi-year leases & anchor tenancies · third-party O&M · utility resale margins (regulatory check required)
Digital / PMO / AM / concession	VBS & data subscriptions · portal fees · PMO & development fees · asset management fees · concession/availability income if structure eventuates (pending)

Cost classes, sensitivities and outputs per audience

COST CLASSES (priced, not guessed)

- EPC capex per WP — from contractor pricing, not benchmarks alone
- Land cost/lease — from confirmed tenure terms (pending)
- Equipment capex and renewal cycles
- Energy (largest cold-chain driver), labour, maintenance, insurance
- Digital opex: licences, SOC, connectivity, refresh cycles
- Concession fees/royalties if applicable (pending)

Audience	Model outputs required
Banks	DSCR profile, gearing, tenor/tail, security coverage
Investors	Equity IRR, payback, dividend profile, exit valuation logic
Government	Jobs, state revenue, trade-facilitation KPIs, fiscal cost of support
Board	Funding plan, milestone cash needs, downside survivability

KEY SENSITIVITIES

- Throughput growth vs verified baselines · ramp-up length · anchor pre-commitment share
- Cross-border rail interchange capture (KTMB–SRT service patterns) · energy tariffs · MYR/THB

11

- Corporate · Land · Project
- Government · Technical
- Financial · Legal · Commercial
- ESG · Operational · Digital

Due Diligence Checklist

Eleven workstreams. Every item answered with documents, not statements — the evidence set for investment committees and bank credit processes.

Workstreams A–E: the existential checks

Workstream	Key items (abridged — full checklist in package document)
A · Corporate	SSM extracts, UBOs, board authorisations, audited accounts, charges & litigation searches, all existing MOUs/agreements with status
B · Land	Titles per parcel (owner, category, conditions) · state/reserve/Malay Reserve status · encumbrances & caveats · zoning · KTMB/Railway Assets Corporation land involvement · flood history
C · Project	Existing studies & master plans · what exists today vs aspiration · prior tenders/liabilities · utilities availability · interface with PIP and legacy terminal operators
D · Government	Written state support · federal engagement status (MOT, MITI, JKDM, UKAS) · NCIA status · KTMB engagement · issued gazettes/licences · Thai-side engagement
E · Technical	Geotech adequacy · rail connection feasibility (gradient, possessions) · road capacity · utility loads (cold-chain power) · flood modelling · EIA screening

Workstream B (Land) is the gating item: nothing proceeds without title verification.

Workstreams F–K: bankability and operability

Workstream	Key items (abridged)
F · Financial	Owner funding capacity · existing financing/liens · tax structure & incentive eligibility · basis of any previously circulated figures (validate or discard)
G · Legal	Rights held vs rights claimed (evidence per item) · foreign investment limits · licensing map (bonded, forwarding, CIDB, CAAM) · sanctions screening of all counterparties
H · Commercial	Verified cargo baseline (KTMB/Customs data requests) · named anchor prospects & commitment status · competing facilities pipeline · tariff benchmarks · demand interviews
I · Environmental & Social	EIA determination · site occupants/displacement · heritage · IFC Performance Standards / Equator alignment · climate resilience
J · Operational	Operating model & candidate operators · labour availability in Perlis · border hours as throughput cap · bonded security requirements
K · Digital	Existing systems · fibre/carrier availability · JKDM interface constraints · PDPA & Cyber Security Act 2024 obligations · vendor landscape

12

- Foundation & land
- Government & commercial
- Structure & finances
- Timeline & process

Questions for the Project Owner

Collaborative, professional questions that help the owner assemble what investors, Shandong, technology partners and banks will ask for anyway.

Twenty-six questions in seven groups (selection)

FOUNDATION

How did the project originate and what exists today? What does success look like in 5 and 15 years?

LAND & RIGHTS

Which parcels, what tenure, any existing agreements? Does any element rely on railway reserve or KTMB land?

GOVERNMENT

Who has been engaged, and is there anything in writing? Any JKDM discussions on bonded/zone status? KTMB response on sidings?

COMMERCIAL

Which cargo flows anchor demand, and on what evidence? How is the platform positioned vs Perlis Inland Port — integration, complement, or competition?

STRUCTURE

What role does the owner wish to retain? What are expectations on ownership and control? Any commitments a consortium must respect?

FINANCES

What has been invested to date and by whom? Expected owner/partner/bank funding split? Any liabilities attached to land or project?

PROCESS

What timeline and external deadlines apply? Openness to structured DD under NDA with a data room? Who is authorised to negotiate?

Tone: these questions accelerate the owner's own fundraising — they are the same list any serious counterpart will bring.


13

- SPV structure
- Roles & candidates
- Agreements map
- Governance principles

Consortium Structure

A single-purpose Malaysian SPV with clean contracts around it — designed to satisfy the $\geq 51\%$ Malaysian ownership floor and lender governance standards.

Proposed SPV structure (percentages deliberately unstated)

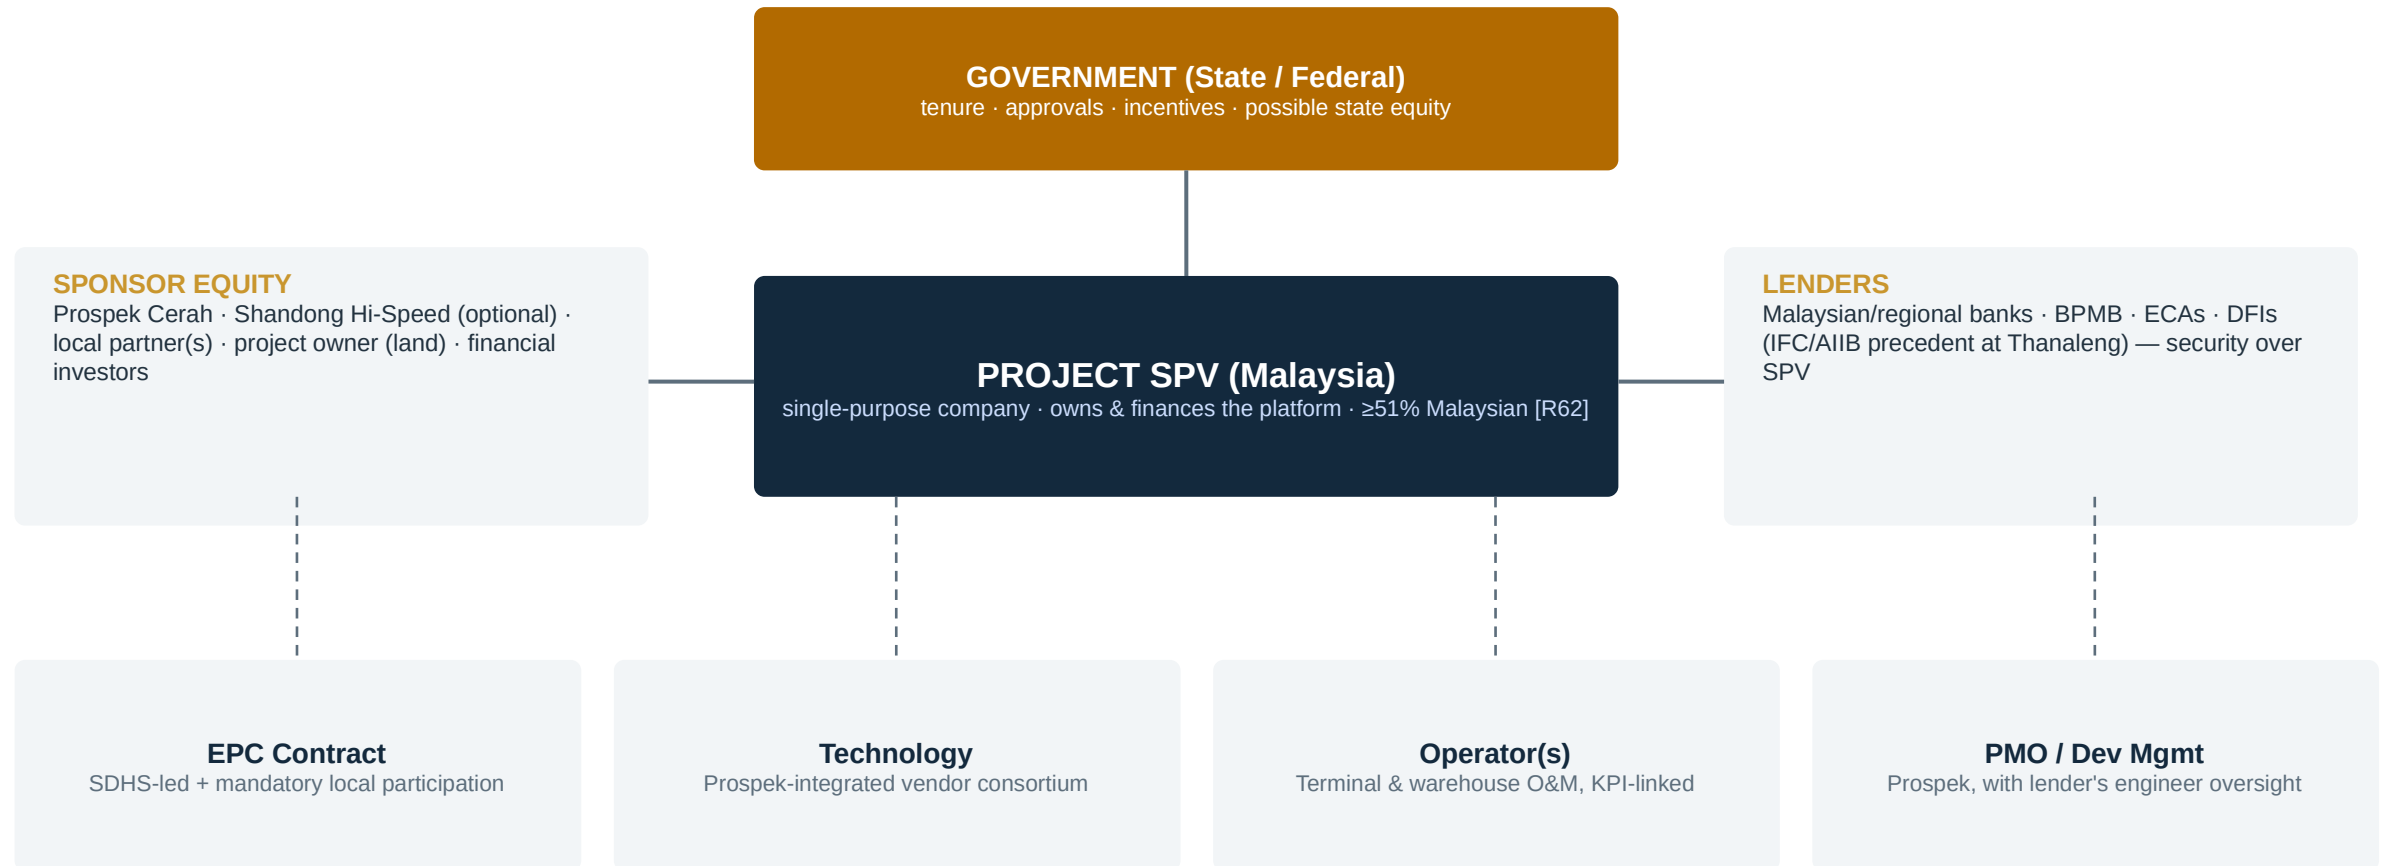

The SPV contracts everything outward; related-party contracts (Prospek services, SDHS EPC) disclosed, benchmarked and approved by non-conflicted directors.

Nine key agreements and four governance principles

#	Agreement
1	Shareholders' Agreement — governance, reserved matters, transfers, deadlock
2	Land lease / SPA / land-for-equity — form follows verified tenure
3	Concession / development agreement with state (if applicable)
4	EPC Contract (FIDIC Silver/Yellow basis for lender-financed EPC)
5	O&M / Terminal Operating Agreement(s)
6	Technology supply, integration and SLA agreements
7	Development Management / PMO Agreement
8	Financing documents — facility, security, lender direct agreements
9	Anchor customer / tenancy pre-commitments

GOVERNANCE PRINCIPLES

- Board proportional to equity, with protective minority rights
- Related-party contracts disclosed, market-benchmarked, approved by non-conflicted directors — essential for lenders and co-investors
- Independent lender's engineer and model auditor at financial close
- ESG and compliance committee from day one — a border/customs environment demands clean governance (the PKFZ lesson) [R79]

14

- Gating risks
- Full register by category
- Mitigation ownership

Risk Register

Twenty-five risks across ten categories, qualitatively scored pre-feasibility. Five are gating: they must be addressed before money moves.

Five gating risks — address before money

R01 · Land & rights	Position weaker than represented; project premise fails	Land DD as Phase 1 gate; zero capital before title verification
R02 · Government support	Not secured, or shifts with political cycles	Written instruments early; multi-party alignment (state + NCIA + federal)
R06 · Demand evidence	Cargo volumes below case; slow ramp	Anchor pre-commitments before financial close; conservative lender case
R09 · Financeability	Greenfield border asset fails to raise acceptable debt	ECA/DFI tracks in parallel; staged capex; strong sponsor equity signal
R15 · Rail connection	KTMB siding approval/possession delays	Early technical agreement; design to operate road-only in interim

Column 3 = mitigation. Ratings are qualitative team judgments at pre-feasibility stage — to be re-scored quantitatively in due diligence.

Register overview: 25 risks across ten categories

Category	Representative risks (L/I at pre-feasibility)	Core mitigations
Government & border	Licences delayed (M/H) · border policy shifts (M/H) · Thai-side lag (M/M)	Early JKDM engagement; design to operate without zone status initially; bilateral corridor dialogues
Commercial	Competition from PIP/BKH/Thai facilities (M/M) · anchor concentration (M/M) · KTMB haulage economics (M/M)	Complement/integrate positioning; tenant diversification; early KTMB commercial MOU
Financial	FX (M/M) · energy escalation vs cold chain (M/M)	Natural hedging; tariff pass-through; solar PV
Construction & technical	Ground/flood conditions (M/M) · EPC overrun (M/H) · interfaces (M/M) · utility capacity (M/M)	Full GI before pricing; fixed-price wrap; single-wrap preference; early TNB application
Technology & operations	Integration failure (M/M) · cyber breach (M/H) · operator underperformance (L/M) · labour gap (M/M)	Open standards + escrow; IEC 62443/ISO 27001 + SOC; KPI O&M with step-in; NCIA training programmes
Political & ESG	Geopolitics (L/M) · sanctions exposure (L/H) · EIA conditions (M/M) · DFI ESG bar (L/H)	Balanced consortium; DD screening + substitution rights; IFC PS-aligned ESMS from Phase 1

15

- Phase plan
- Governance gates
- First 90 days

Roadmap

Seven phases, five governance gates. Indicative durations only — the critical path runs through land verification and government process.

Seven phases from due diligence to operations



Phases 1–2 overlap deliberately: consortium conversations begin during due diligence, but no party commits capital until Gate G1 clears.

Five governance gates — and the first 90 days

Gate	Decision	Evidence required
G1	Proceed past DD	Clean land/rights, government support signals, demand baseline
G2	Sign consortium	Positive feasibility, aligned partners, heads of terms with owner
G3	Financial close	Bankable package: contracts, approvals, committed funding
G4	Notice to proceed	EPC signed, land access, insurance, CPs met
G5	Open for operations	Commissioning complete, licences in force, operator ready

FIRST 90 DAYS

- Execute NDA + information request (Section 11 list) with project owner
- Land title searches and encumbrance checks
- Owner workshop on the 26 questions (Section 12)
- Soundings: state government, NCIA, KTMB, JKDM
- Brief Shandong Hi-Speed on posture options (Section 8)
- Commission cargo demand scan and PIP positioning study
- **Output: Red Flag Report → G1 go/no-go**



- Photo & map plan
- Assumptions A01–A24
- References R1–R82

Appendix

Visual asset recommendations · assumptions register · consolidated references.

Visual asset plan: photos, maps and icons for the final deck

Asset	Recommendation	Source / rights note
Hero photo	Padang Besar station rail yard with freight wagons at dawn; alternative: ASEAN Express launch imagery	Commission photographer on site visit; Bernama/KTMB imagery requires licence
Border imagery	ICQS complex approach, truck queue (illustrates the marshalling case)	Site visit photography; avoid security-sensitive angles — clear with ICQS authorities
PIP context	Perlis Inland Port gate/yard (establishes the incumbent honestly)	Mutiara Perlis/NCIA press assets with permission
Corridor map	Peninsular map: Padang Besar–Penang–Klang rail spine + Hat Yai–Bangkok–Laos–China; inset: border-town detail	Redraw from OpenStreetMap (ODbL attribution) — do not screenshot Google Maps
Site plan	Only after owner confirms parcels — placeholder schematic until then	Owner survey data; licensed surveyor output
Icons	Single-line style (rail, truck, warehouse, snowflake, shield, satellite) — one family throughout	Licensed icon set (e.g., Streamline/Noun Project licence)
Drone footage	Construction-phase progress films for investor updates (Phase 5)	CAAM permit required near border zone — check restricted airspace

Assumptions register (1 of 2): A01–A12

#	Assumption	Class
A01	A defined project exists with an owner able to grant land/rights	Owner
A02	Sufficient land near border/rail can be secured on lender-acceptable tenure	Owner
A03	Project can position as complement/integrator to Perlis Inland Port	Owner/Market
A04	KTMB will agree to siding connection and commercial services	Government
A05	Customs/bonded/FCZ licensing obtainable for the site	Government
A06	Border cargo demand keeps growing in line with verified trends	Market
A07	Cold-chain white space exists at the border	Judgment/Market
A08	Truck marshalling services are monetisable against border hours	Judgment/Market
A09	Shandong Hi-Speed would consider EPC and/or equity roles	Owner
A10	Prospek Ceraf can evidence capability for its eight roles	Owner
A11	Consortium can satisfy 51% Malaysian floor + Bumiputera conditions	Government
A12	Project financing achievable given BPMB/IFC/AIIB precedents	Market

Assumptions register (2 of 2): A13–A24

#	Assumption	Class
A13	The 20-WP breakdown matches final master plan scope	Judgment
A14	Digital systems can interface with JKDM systems at reasonable cost	Government
A15	Indicative phase durations achievable if gating items clear	Judgment
A16	State support for additional logistics investment is obtainable	Government
A17	Border Economic Zone will produce usable incentives	Government
A18	SRT Hat Yai–Padang Besar double-tracking proceeds on reported timeline	Government/Market
A19	Qualitative risk ratings reflect the true pre-feasibility profile	Judgment
A20	No adverse existing agreements encumber the project or site	Owner
A21	Thai counterparts cooperate on corridor improvements	Government
A22	Published PIP figures are broadly accurate despite source conflicts	Judgment
A23	Financial model structure covers all material categories	Judgment
A24	Consortium roles map is negotiable to signature without structural change	Judgment

References (1 of 2): border, rail, PIP, trade

- R1–R5 Border town, station, juxtaposed controls, operating hours — Wikivoyage; Border Crossing Hub; Wikipedia (Padang Besar railway station); FMT (2017); Mekong Region guide
- R6–R8 Roads — Wikipedia FT7/FT79; paultan.org (BKH–Sadao road, 10 Jul 2026)
- R9–R13 Rail & services — China Daily (gauge); KTMB Kargo; The Star (block train 2022; ASEAN Express 2024); railmarket.com (STC, Dec 2025)
- R14–R28 Perlis Inland Port — The Edge; The Star (25 Mar 2025); Railway Gazette (13 Apr 2025); Bernama (30 May 2026); BPMB; NCER; MIDA; FMT (14 Jul 2026); Harakah Daily; RMCD; WCO News; CAREC; Citaglobal reports
- R29–R41 Rail policy & PIP ecosystem — KTMB ETS; Nation Thailand (Thanaleng gauge, SRT double-tracking); FMT; SCMP; Malay Mail (13MP rail); ANN; NST (Kalmar); The Edge (GDC, Maritime Corridor); MIDA (MOU/MOC); Business Today (Berjaya)
- R42–R51 Border & trade — Thai PRD; Malaysiakini; Singapore Customs (ASW); ACTS portal; MITI (JTC US\$30bn); Nation Thailand (trade 2024/2025, checkpoint values); Thairath; KLSE Screener; The Star (Penang 70%)

Full citation list with URLs: docs/17_references.md in the package repository.

References (2 of 2): policy, Perlis, Shandong, benchmarks

- R52–R55 ASEAN & corridors — ASEAN Connectivity Strategic Plan 2026–2035; ADB (IMT-GT); Wikipedia (Kunming–Singapore); Bangkok Post (Land Bridge)
- R56–R63 Federal & rules — NCER/NCIA; MIDA (CVIA); PMO (NTP 2019–2030); MOT (LTFM); Malay Mail (Border Economic Zone; 51% ports rule); UKAS/The Star (PIKAS 2030); MITI (equity conditions)
- R64–R65 Perlis state — Malay Mail (2026 budget); Perlis state portal (growth areas)
- R66–R74 Shandong Hi-Speed — Wikipedia; Baidu Baike (flagged company-published); Devex; Xinhua Silk Road (Qilu); Alpha Spread (000498.SZ); CSI/CTOS record; The Star & The Edge (PTT Synergy, Sep 2025); Moody's (2018 A3)
- R75–R82 Benchmarks & financing — IFC & AIIB (Thanaleng); UNESCAP (Lat Krabang, Malaysian dry ports); ResearchGate; The Edge (PKFZ); AIIB (US\$6bn Malaysian bank partnership); Sime Darby Property/Mingtiandi (LOGOS fund)

Citation-quality note: aggregator and trade-press items are flagged in text and must be replaced with primary documents (Bursa filings, gazettes, audited statements) during due diligence.

NEXT STEP

One meeting with the project owner unlocks everything else.

- The corridor thesis is verified; the project's rights are not — Phase 1 due diligence resolves that in 3–6 months at development-capital cost only
- The 26 owner questions and 11 due-diligence workstreams in this package are the agenda for that meeting
- No capital, no commitments and no representations until Gate G1 clears

This document contains no representation of ownership, concession, operating rights or licences. All items not publicly verified are pending confirmation from the project owner.
